Georgetown Divide Public Utility District

Update No.17 ♦ Sept 30, 2018
Agenda Item 6.E.

AUBURN LAKE TRAILS WATER TREATMENT PLANT

PROJECT UPDATE

UPCOMING ACTIVITIES:

- Filter Bldg.- Finalize pipe connections and electrical
- Filters – Connector Pipes
- Raw Water Pump Station – Painting and finalize Electrical
- Backwash Water Recovery – Mods to Existing Clarifier

COMPLETED ACTIVITIES:

- Raw Water Siphon
- Temporary Finish Water Bypass Line
- Filter Bldg.- Footings, Slab and Exterior Building
  Chlorine Contact Basin with Baffles
- Raw Water Pump Station Footing, Slab & Building
- Concrete Pour – Sludge Drying Beds- Slab & Walls

GEORGETOWN DIVIDE PUBLIC UTILITY DISTRICT
6425 Main Street
P.O. Box 4240
Georgetown, CA 95634
www.gd-pud.org **(530) 333-4356**
Steven Palmer, PE,
General Manager
For additional information, contact:
George Sanders, Project Manager,
at gsanders@gd-pud.org or
Call (530) 333-4356

CONTRACT UPDATE:

Original Contract Amount:	$ 10,249,000	
Contract Change Order #1:	$ 39,772	
Contract Change Order #2:	($ 970)	
Contract Change Order #3:	No Cost	
Contract Change Order #4:	$ 12,184	
Contract Change Order #5:	$ 20,922	
New Contract Amount		$10,320,908
Expended thru September 2018		$9,137,571
Percent Complete		89%
Anticipated Completion Date		December 2018
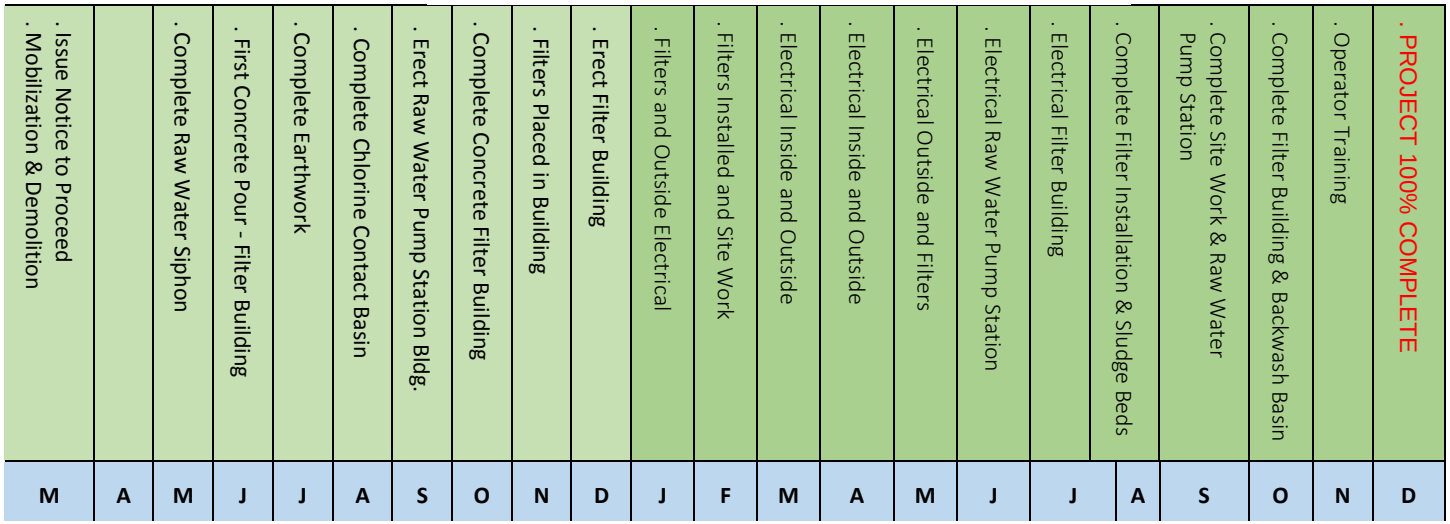
PROJECT CONSTRUCTION SCHEDULE
